

FRIDAY, JUNE 14, 2024



PROGRESS MADE THIS WEEK MONDAY-FRIDAY [06.10-06.14]

- ◆ Soil cell and electrical work along Pennsylvania [Main to Park]
- ◆ Asphalt milling in the project's west end

WORK ANTICIPATED NEXT WEEK MONDAY-FRIDAY [06.17-06.21]

- ◆ Roadway excavation on Prospect's west side [Pennsylvania to Duane]
- ◆ Planter curb foundations along Pennsylvania [Main to Park]
- ◆ Stand electrical poles along Pennsylvania's south side [Main to Park]

DETOUR INFORMATION

Pennsylvania [Forest to Park] is currently ONE-WAY WESTBOUND.

Prospect [Pennsylvania to Duane] will be ONE-WAY NORTHBOUND intermittently next week; see the [detour route map](#).

ALL businesses and pedestrian access remain open.

OTHER IMPORTANT INFORMATION

- ◆ Equipment issues have deferred Prospect roadway excavation to Monday, June 17.
- ◆ Sidewalk work is on the horizon for the east end of Pennsylvania; it is tentatively scheduled for the week of June 24th.
- ◆ *If you ever have questions/concerns regarding the project, please reach out to a contact listed below.*



downtownge.com



Clay Keller, P.E.
Meredith Hannah




630-936-9456
630-547-5345







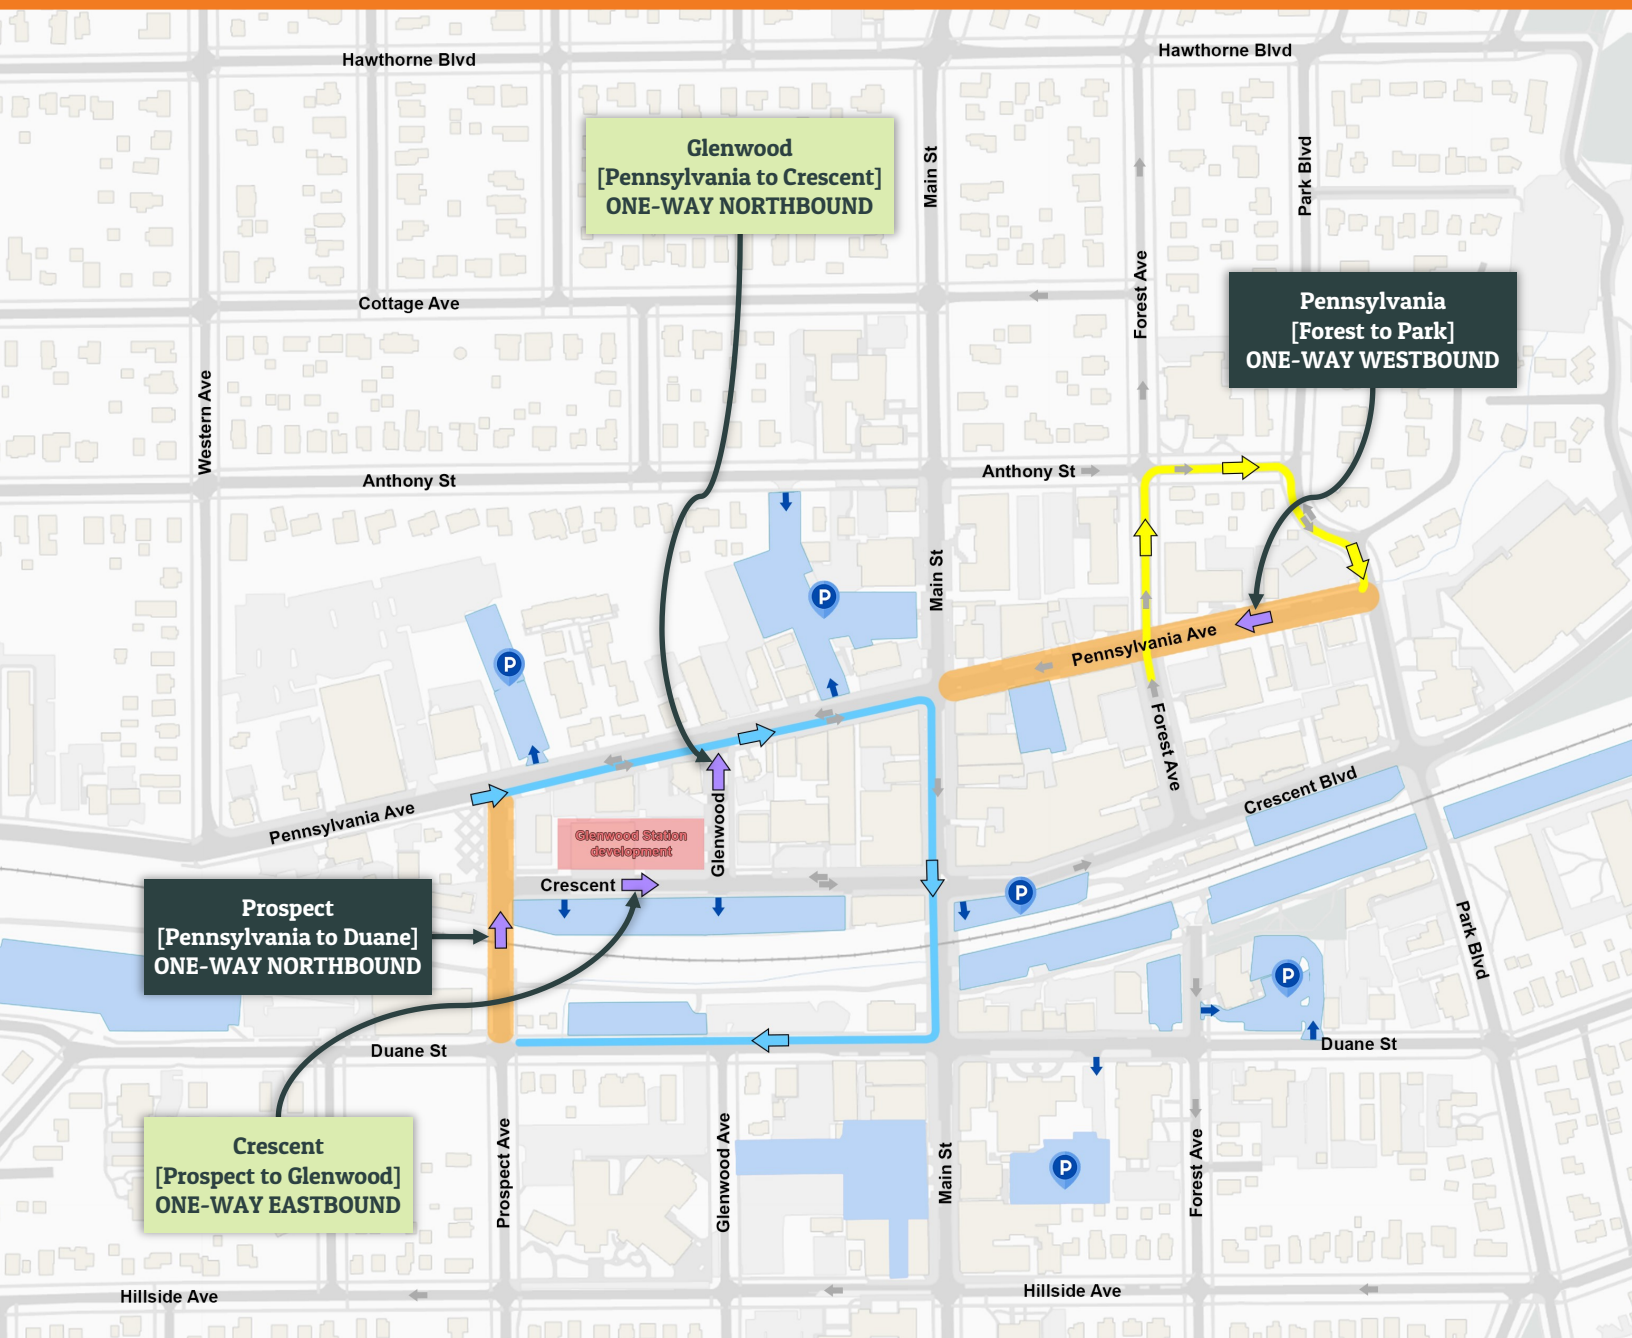

pkeller@bla-inc.com
mhannah@glenellyn.org





BLUE AREAS INDICATE NEARBY PARKING LOTS
WITH SHORT-TERM CUSTOMER PARKING
FOR MORE INFO, VISIT: GLENELLYN.ORG/PARKING

	CONSTRUCTION WORK ZONES		NB PROSPECT DETOUR		PARKING ENTRANCE
	EB PENNSYLVANIA DETOUR		SB PROSPECT DETOUR		CHANGE TO ONE-WAY

